ID		Task Name	Duration	Start	Finish
1		**ZOO PARKING**	**639 days**	**Wed 10/12/16**	**Mon 3/25/19**
2		First Steering Committee Meeting	0 days	Thu 10/13/16	Thu 10/13/16
3		Review Draft RFQ (Request for Qualifications)	0 days	Thu 10/13/16	Thu 10/13/16
4		Review Draft Schedule	0 days	Thu 10/13/16	Thu 10/13/16
5		Committee to establish weighted rating criterias	0 days	Thu 10/13/16	Thu 10/13/16
6		**Discuss Communication Plan**	**1 day**	**Wed 10/12/16**	**Wed 10/12/16**
7		Establish Website	1 day	Wed 10/12/16	Wed 10/12/16
8		Upload draft RFQ, Draft Schedule	1 day	Wed 10/12/16	Wed 10/12/16
9		Information in Website	1 day	Wed 10/12/16	Wed 10/12/16
10		**Finalized RFQ and and prepare advertisement docs**	**3 days**	**Thu 10/13/16**	**Mon 10/17/16**
11		Prepare advertisement documents	2 days	Thu 10/13/16	Fri 10/14/16
12		Upload Finalized RFQ	1 day	Mon 10/17/16	Mon 10/17/16
13		Advertise RFQ	40 days	Tue 10/18/16	Mon 12/12/16
14		Distribute RFQ to Steering Committee Members for rating	10 days	Tue 12/13/16	Mon 12/26/16
15		**Second Steering Committee Meeting**	**5 days**	**Mon 12/26/16**	**Mon 1/2/17**
16		Compile/Discuss Rating	0 days	Mon 12/26/16	Mon 12/26/16
17		Selection of Design Team (Top 3?)	0 days	Mon 12/26/16	Mon 12/26/16
18		Steering Committee decides presentation (Top 3?)	0 days	Mon 12/26/16	Mon 12/26/16
19		Top 3 Design Team Presentation	5 days	Tue 12/27/16	Mon 1/2/17
20		Fund raise and acceptance of design funds	90 days	Thu 10/13/16	Wed 2/15/17
21		Request for Proposal (RFP) & Schedule from selected Design Team	5 days	Tue 1/3/17	Mon 1/9/17
22		Execute Contract	40 days	Tue 12/27/16	Mon 2/20/17
23		Consultant Design	180 days	Tue 2/21/17	Mon 10/30/17
24		Fund raise and acceptance of construction funds	180 days	Tue 2/21/17	Mon 10/30/17
25		Construction (Phasing?)	365 days	Tue 10/31/17	Mon 3/25/19

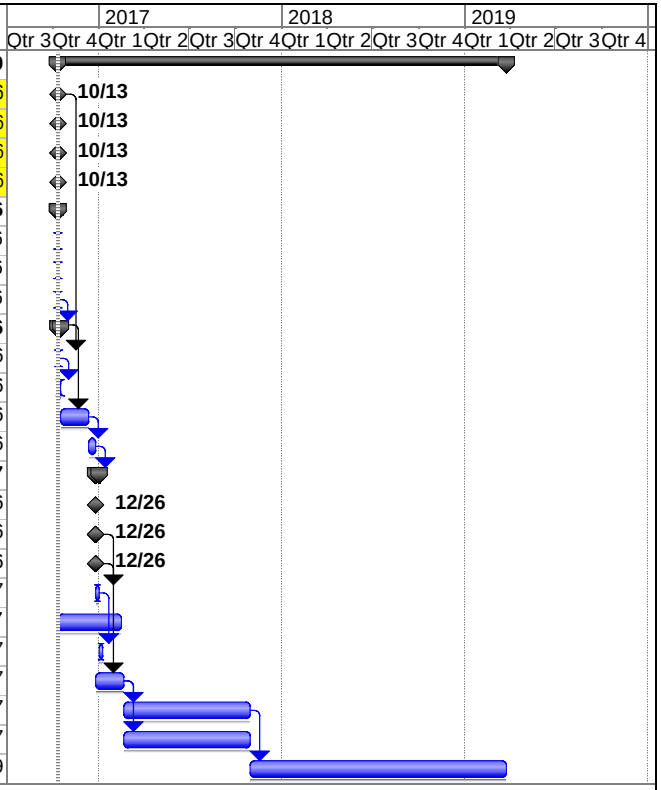

DRAFT

INFORMATION ONLY

Project: Zoo Parking
Date: Mon 10/10/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
